

Rehabilitation / Improvement of
road from Bhera Malikwal
Shahpur Sahiwal road Section
Jhawarian to Shahpur Length
18.50 Km District Sargodha

Yellow

1st Monitoring Report

Rana Umar Shafiq
Assistant Director
19-Jul-2025

PROJECT PROFILE

Scheme No	01332308214
GS NO	1773
Location	Shahpur, Sargodha
Sub-Sector	Roads
PC-I Cost	1481.194M
Expenditure	363.000M
Planned Start Date	01-Jul-2024
Planned End Date	30-Jun-2026
Project Type	Single

PROGRESS ANALYSIS

Planned Physical Progress *	51.99%
Actual Financial Progress **	24.51%
Actual Physical Progress ***	31.23%

* $(\text{Visit Date} - \text{Planned Start Date}) / (\text{Planned End Date} - \text{Planned Start Date}) * 100$

** $(\text{Expenditure} / \text{PC-I Cost}) * 100$

*** Please Refer to WBS Section (8) of Report



Directorate General
Monitoring & Evaluation



DGME-Real Time Monitoring & Evaluation System



042-99233177-91



info@dgmepunjab.gov.pk

4th & 5th Floor, 65-Trade Centre Block, M.A Johar Town, Lahore

Copyright © All Rights Reserved - DGM&E

Table of Contents

1. Disclaimer	2
2. Project Profile	2
3. Progress Analysis	3
4. Detailed Analysis	3
5. Financial Analysis	4
6. Earned Value Analysis	4
7. Design & Scope	5
8. Work BreakDown Structure	6
9. Work BreakDown Structure Summary	7
10. Test/Reports Summary	7
11. Monitoring Rating Index	7
12. Observation & Recommendations	10
13. Stakeholders	12
14. Work BreakDown Structure & Test Results (Gallery) / Work in Progress	12



1. Disclaimer

This information is solely for sponsoring and executing agencies for course correction. The content of this report cannot be quoted in media, court, and any other forum.



2. Project Profile

Rehabilitation / Improvement of road from Bhera Malikwal Shahpur Sahiwal road Section Jhawarian to Shahpur Length 18.50 Km District Sargodha	
Scheme No	01332308214
Objectives	Road has outlived its normal / designed life due to running of traffic more than its normal capacity. To facilitate transporters while transporting their produce to the market. The proposed road will facilitate the inhabitants of the area and will help a lot in uplifting their socio economic standard of life
GS NO	1773
Location	Shahpur, Sargodha
ADP Sector	Infrastructure Development
Sub-Sector	Roads
Sponsoring Ministry/ Agency	Government of Punjab
Execution Agency	Communication & Works Department
PC-I Cost	1481.194M
Administrative Approval	03-Jul-2024
Expenditure	363.000M
Planned Start Date	01-Jul-2024
Planned End Date	30-Jun-2026
Actual Start Date	02-Aug-2024
Approving Forum	PDWP
Contractor	M/s JKG
Design Engineer	C&W
Resident Supervision	NESPAK
TPV Consultant	ESSIAAR
RE Hired Date	24-08-2024
Work Order Date	02-08-2024
Gestation Period	
Visit Date	15-Jul-2025




3. Progress Analysis

Planned Physical Progress	Actual Financial Progress	Actual Physical Progress	Planned Physical Progress vs Actual physical Progress	Actual physical Progress vs Actual Financial Progress
51.99%	24.51%	31.23%	-18.51% Ahead of Schedule	45.99%

4. Detailed Analysis

Visit Date	Officer Name	Visit Location	Contractor	Resident Engineer	Planned Physical Progress	Actual Financial Progress	Actual Physical Progress	Monitoring Rating Index
25-Jun-2025	Zainab Tariq	Sargodha	M/s GKG	NESPAK	49.25%	24.51%	12.00%	50 Yellow
15-Jul-2025	Quratul Ain	Sargodha	M/s JKG	NESPAK	51.99%	24.51%	97.72%	57 Yellow

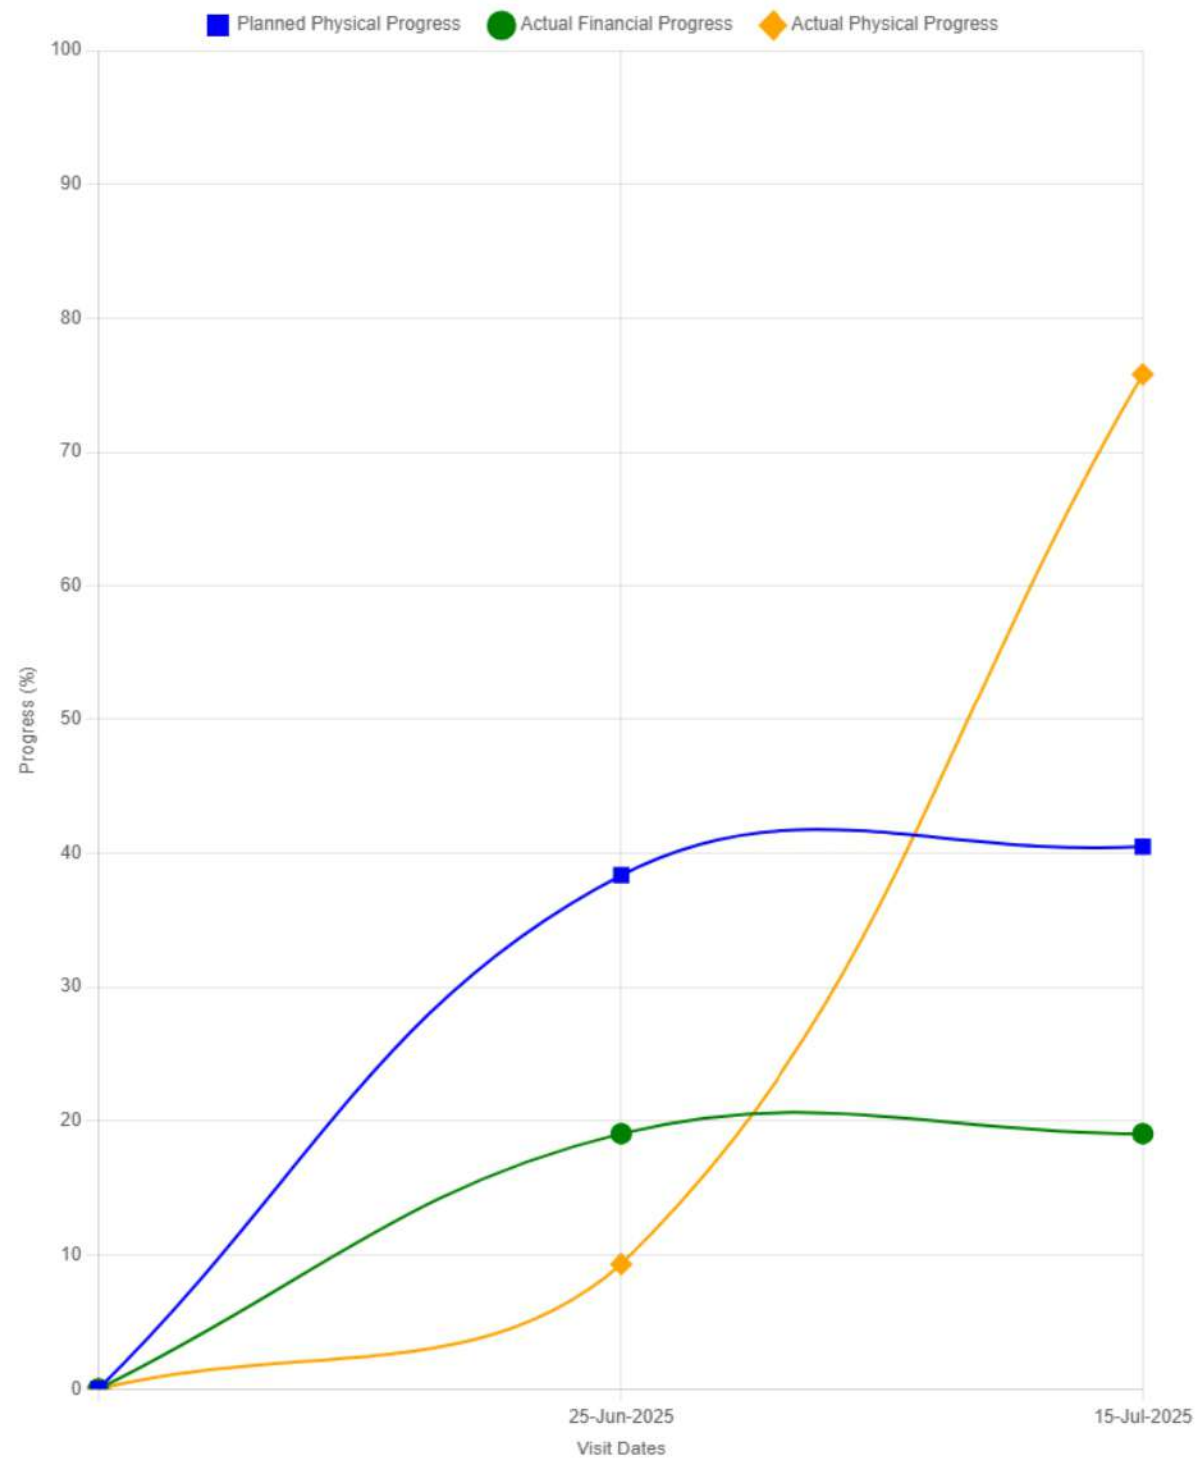

5. Financial Analysis

5.1 SMDP Information

Fiscal Year	Allocation (M)	Releases (M)	Utilization (M)	Release/Allocation	Utilization/Releases
2023-2024	0.10	0.00	0.00	0.00%	0.00%
2024-2025	713.00	713.00	363.00	100.00%	50.91%
Total	713.10	713.00	363.00	99.99%	50.91%

5.2 Information Provided by Department.

Total	713.10	713.00	363.00	99.99%	50.91%
-------	--------	--------	--------	--------	--------

6. Earned Value Analysis

Items		Remarks
Project Cost	1481.19	Project Cost (m)
Percent Completed [Physical]	70.50%	Physical progress (%)
Planned Value or BCWS	769.92	Budgeted Cost of Work Scheduled
Earned Value or BCWP	1044.24	Budgeted Cost of Work Performed
Actual cost of work performed (ACWP)	363.00	Current financial progress
Scheduled Variance (SV)	274.32	Ahead of Schedule
Cost Variance (CV)	681.24	Within The Budget
Schedule Performance Index (SPI)	1.36	On Schedule as SPI is greater than 1
Cost Performance Index (CPI)	2.88	Within Budget as CPI is greater than 1
Estimate Cost at Completion	799.95	Project with in Budget
Estimate Cost to Complete	436.95	Further funds required for completion at current pace of works
Earned Schedule (ES)	17	Equivalent progress of 16.88 months achieved till date against planned 0 months
Time Variance (TV)	4.43	Project On Track
Time Estimate at Completion (TEAC)	17.66	Months

Alert

Earned Value Analysis shows that the project would not face either time or cost overrun if the work pace is not interrupted.

7. Design & Scope

Description	Quantity	Description	Quantity
i. Formation width	40 ft	v. carpet	2" 1.5" inches
ii. Metalled width	4 20 4 ft	vi. TST	4 ft
iii. sub base	4" 6" 12" ft	vii. Tuff pavers	60 Nos
iv. base	8" 12" ft	viii. Rigid	10 inches



8. Work BreakDown Structure

8.1- Work BreakDown Structure (RRP)

WBS Name:

WBS Weight: 100.00%

PC-I Components	Weight	Physical Progress			Test/Reports					
		Activity	To be Achieved	Achieved	Contractor		RE		TPV	
					Pass	Fail	Pass	Fail	Pass	Fail
8.1.1 Main Carriageway/Formation	60.0%	DST/TST/Asphalt/Prime Coat/Tack Coat	15.0%	6.00%	0	0	19	0	13	0
		Base/Overlay/Reconstruction/WBM	25.0%	10.50%	0	0	0	0	167	18
		Sub base	10.0%	3.90%	0	0	0	0	149	14
		Earthwork/Berm	10.0%	3.50%	0	0	0	0	118	17
		Total	60.00%	23.90%	0	0	19	0	447	49
8.1.2 Structural Works/Culverts/Drains/Bridges	30.0%	Concrete/Rigid	15.0%	2.40%	0	0	0	0	281	0
		RCC/Steel Work	8.0%	2.48%	0	0	0	0	2	0
		Brickwork	7.0%	2.45%	0	0	0	0	0	0
		Total	30.00%	7.33%	0	0	0	0	283	0
8.1.3 Road Furniture	10.0%	Kerb Stone/KM Stone	4.0%	0.00%	0	0	0	0	0	0
		Tuff Tiles	3.0%	0.00%	0	0	0	0	0	0
		Lane Marking/Boards/Cat Eyes	3.0%	0.00%	0	0	0	0	0	0
		Total	10.00%	0.00%	0	0	0	0	0	0
Grand Total	100.0%			31.23%	Pass:	749			Fail:	49

Weightage	Weightage Out of 100	WBS Formula	Achieved
100.00%	31.23%	(31.23/100) x 100.00	31.23%



9. Work BreakDown Structure Summary

WBS Names	To be Achieved Progress	Achieved Progress
1.	100.00%	31.23%
Total	100.00%	31.23%



10. Test/Reports Summary

Test/Reports	Pass	Fail	Total	Fail (%)
Contractor	0	0	0	0%
RE	19	0	19	0%
TPV	730	49	779	6%
Total	749	49	798	6%

11. Monitoring Rating Index

Criteria	maximum Points	Points Obtained
1. Planning (10%)		
P1.1 Feasiblity Study	5	
Yes	5	
No	0	0
P1.2 Project objectives defined and SMART	5	
Yes	5	5
No	0	
P1.3 Implementation Schedule (Gant Chart) Present	5	
Yes	5	
No	0	0
P1.4 Financial phasing given	5	
Yes	5	5
No	0	
P1.5 Result Base Monitoring Framework	5	
Yes	5	
No	0	0
P1.6 Project Justification/Need Assessment	5	
Yes	5	5
No	0	
Total	30	15
((Points Obtained in Performance / 30) * 100) * 0.1		5
2. Execution (30%)		
P2.1 Project schedule being followed?	5	
Yes	5	5

Criteria	maximum Points	Points Obtained
No	0	
P2.2 Is allocation of funds as per phasing?	5	
Yes	5	5
No	0	
P2.3 Revisions of PC-1	10	
No Revision	10	10
One Revision	7	
two Revision	5	
three Revision	2	
More than three revisions	0	
P2.4 Provision of Documents w.r.t Hiring, Procurement, Training, Tenders & Bidding, etc.	5	
Provided	5	5
Partially Provided	2.5	
Not Provided	0	
P2.5 Internal Monitoring Conducted by Sponsoring Department	5	
Yes	5	
No	0	0
P2.6 Executing Agency representative present on site	5	
Yes	5	5
No	0	
Total	35	30
((Points Obtained in Performance / 35) * 100) * 0.3		26
3. Performance (60%)		
P3.1 Difference of Planned & Physical Progress (%)	10	
Lesser than 10%	10	10
Between 10% to 20%	5	
Greater than 20%	2	
P3.2 Schedule Performance Index (SPI)	5	
Greater than 1	5	5
Equal to 1	2.5	

Criteria	maximum Points	Points Obtained
Less than 1	0	
P3.3 Cost Performance Index (CPI)	5	
Greater than 1	5	5
Equal to 1	2.5	
Less than 1	0	
P3.4 Failed Tests (Contractor, RE, and TPV) % of total Tests performed	5	
Fail Tests (Less than 5%)	5	
Fail Test (Greater than 5% & less than 10%)	2.5	2.5
Fail Tests (Greater than 10%)	0	
Data Not Available	0	
P3.5 Critical issues in Project	20	
No Critical Observations	20	
1-2 Critical Observations	10	
More than 2 Critical Observation	0	0
P3.6 Beneficiary Feedback		NA
Over 70% Satisfaction level	5	
Between 50% to 70% Satisfaction Level	2.5	
Less than 50% Satisfaction level	0	
Total	45	22.5
((Points Obtained in Performance / 45) * 100) * 0.6		30
Planning + Execution + Performance	Total	61
Overall Project Rating	35-70 Points	Average
Rating Parameters		
Above 70 Points		Good
35-70 Points		Average
Below 35 Points		Critical

Observations	Photos
Observation 1 Critical (Absence of Dewatering and Stormwater Management Measures) No provision for dewatering or temporary drainage arrangements has been observed at the site. In the event of rainfall, the lack of sump pumps, proper slope grading, or temporary drainage channels may result in water accumulation within the excavation pit. This can lead to subgrade instability, delay in construction, or collapse of side walls due to hydrostatic pressure buildup.	
Observation 2 Critical (incomplete shoulder) It has been observed that the adjoining shoulders are unfinished, unpaved, and composed of loosely compacted earth. This condition compromises the essential lateral confinement for the rigid pavement, increasing the risk of edge stress concentration and potential longitudinal cracking due to unbalanced vehicular loading and lack of structural restraint.	
Observation 3 Critical (Significant Delay in Physical Completion:) It has been observed that despite full financial expenditure against the FY 2024–25 allocation and 86% overall budget utilization, the physical progress of the project remains markedly behind schedule. Although the contractual completion date was June 30, 2025, substantial portions of the work such as incomplete pavement layers and continued earthwork activities demonstrate that the project is far from achieving its intended completion. This discrepancy reflects a significant inefficiency in the conversion of financial resources into corresponding physical outputs, indicating potential shortcomings in project execution and monitoring.	
Observation 4 Medium (Drain work under construction) The excavation site lacks proper barricading and hazard demarcation, which poses a serious safety risk to road users and pedestrians. (As Shown in Figure 1)	

Figure 1: Drain work under construction

Name	Designation	Contact Number	Department
M.Ghulpham	XEN	03217360436	Highways Department & C&W



14. Work BreakDown Structure & Test Results (Gallery) / Work in Progress

8.1- WBS Name:

8.1.1. Main Carriageway/Formation



Sub base [3.90% / 10.0%]

Earthwork/Berm [3.50% / 10.0%]

Contractor

RE

TPV



Contractor

RE

TPV



8.1.2. Structural Works/Culverts/Drains/Bridges



Brickwork [2.45% / 7.0%]

Contractor

RE

TPV

Pass

